

SDCCD MEASURE HH BOND PROGRAM PROJECT PROFILE — SAN DIEGO MIRAMAR COLLEGE BUILDING A200

Project Teams

General Contractor	TBD
Architect	Lance Lareau
Structural Engineer	Miyamoto International
Civil Engineer	N/A
Mech./ Elect. Engineer	Shadpour Consulting
Executive Const. Manager	Steve Evanco

Project Schedule


Programming Complete	Design and DSA Approval	Construction Completion (Est.)	FFE & Move-In (Est.)
09-01-2025	N/A	TBD	N/A

Current Status/Phase: Design Phase

Project Features

- Replace the existing packaged air-conditioning unit.
- Existing unit is located on an existing concrete pad.
- Unit serves the mat room training area of the police academy.
- New unit will be appropriately sized to meet the room’s load requirements.
- Design will be based on a readily available replacement packaged AC unit.

Project Map

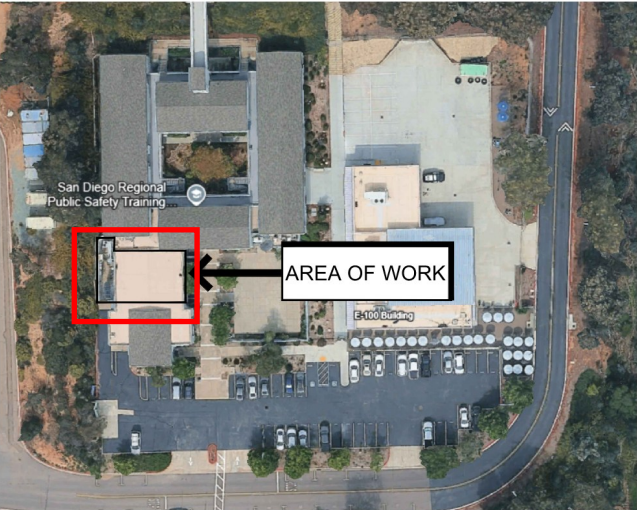

10440 Black Mountain Rd, San Diego, CA 92126



Project News & Information

Additional resources, articles, and links related to this project will appear here when available. For comprehensive information about Measure HH and all ongoing projects, please explore [the Measure HH website](#).

Project Insights

The project replaces an existing packaged ac unit that is located on an existing concrete pad that serves the mat room training area for the police academy.

- Upcoming Milestones:
- Contract and Notice to Proceed (NTP) issued to Shadpour Consulting Engineers: November 18, 2025
 - 95% Schematic Design Package for the Police Academy Bldg. A200 MAT Room HVAC Mechanical Design: December 24, 2025
 - Anticipated bidding for the project February 2026
 - Contract award anticipated March 2026

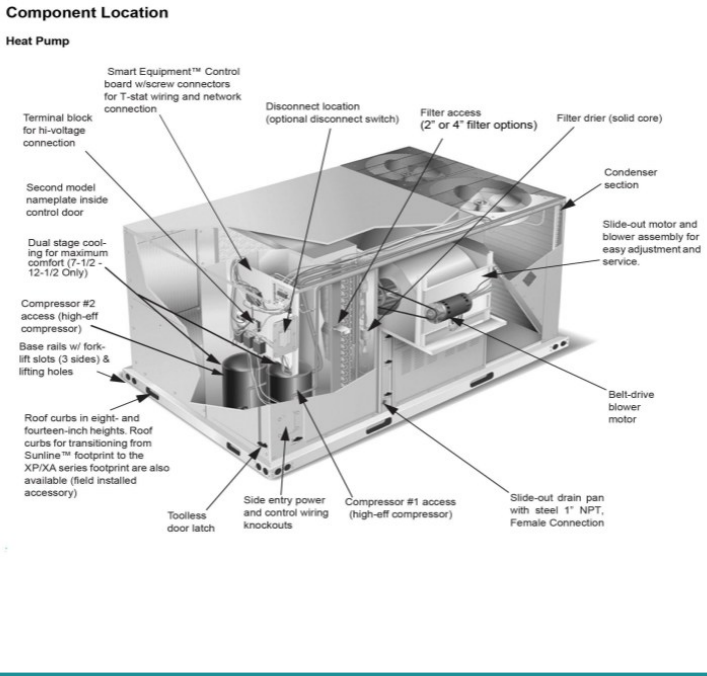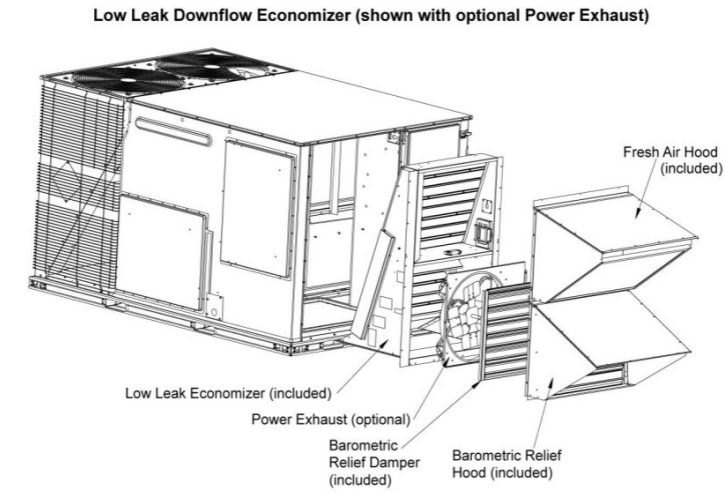

Replace HVAC, AHU ALC Controls Units				Classic Schedule Layout			
Activity ID	Activity Name	Schedule % Complete	Original Duration	Remaining Duration	Actual Duration	Start	Finish
Replace HVAC, AHU & ALC Controls Units		0%	249	249	0	01-Jul-25	12-Jun-26
A1000	Funding	100%	1	1	0	01-Jul-25	01-Jul-25
A1010	Planning	41.86%	43	43	0	02-Jul-25	29-Aug-25
A1020	Design	0%	44	44	0	01-Sep-25	30-Oct-25
A1030	Design Approval	0%	5	5	0	03-Nov-25	07-Nov-25
A1040	Procurement	0%	23	23	0	10-Nov-25	10-Dec-25
A1050	Construction	0%	108	108	0	11-Dec-25	11-May-26
A1060	Close-Out	0%	24	24	0	12-May-26	12-Jun-26
